

SPLOST Construction

► MORROW HIGH • PG. 1

► MICHELLE OBAMA STEM • PG. 2


► JONESBORO HIGH & UPCOMING PROJECTS • PG. 3

Morrow High




It was last January that our Clayton County Public Schools' Board approved the new Morrow High Replacement. What a difference a year makes. While the year of 2020 did present some challenges, onsite it is clear to see that Morrow High's progress remained steady. Steel erection at both the education building, gym building and their connecting bridge is 95% complete. The colossal size of the new facility is very much apparent. The slab on grade (1st floor) has been poured for the entire facility. In the three story Education Building, the slab on deck has been poured at two of the three sequences of both the 2nd and 3rd floors. With the concrete slabs poured, HVAC ductwork as well as fireproofing, plumbing and electrical rough-ins have taken place. All of this have been the precursors for the masons, who over the past couple of weeks have flooded the project on all three floors. You can now see the openings forming for the many windows that will be soon be a part of this grand facility. Over at the gym building, the slab on deck is scheduled to be poured in the next couple weeks, once the small remaining steel is erected. However, plumbing and electrical rough-ins have already begun. Lastly, the school buildings are not the only facilities that have progressed. All four parking lots have curb and gutter and received either asphalt or a base course and the new Stadium's footings for its grandstands have been poured. The Perkins+Will designed new Morrow High and Stadium is scheduled for completion in 2022 and is being performed by MEJA Construction.

Michelle Obama STEM

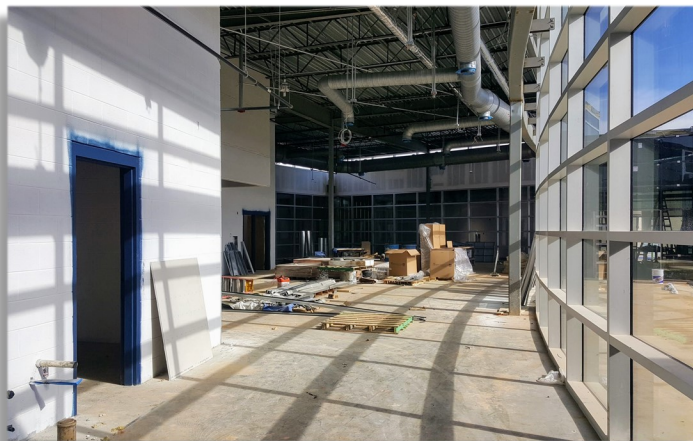


We are just 6 months away from the completion of Michelle Obama STEM Elementary Academy. And the finish line is definitely within reach. All CMU and brick installation has wrapped up at the facility. Window installation is now complete with the exception of just the gym. Additionally, roofing has made great progress at the new facility. The administrative area, cafeteria, media center and 3rd grade classroom wing is fully complete while lightweight concrete is complete in the remaining corridors. With these areas dried-in, painting has begun as well. Not only are the walls and door frames being painted but the stage is beginning to be painted black from floor to ceiling for a true theater aesthetic while the ceiling of the cafeteria has been painted blue. Outside of the facility, HVAC units are being hoisted to the roof and the separate parent & bus drop-off areas'. Over at the new bus facility site, underground rough-ins are complete and preparation for pouring the slab on grade for the office building is scheduled for next week. Grading for the new site for the parking lots and fueling station is ongoing due to the discovery of rock onsite. Both facilities are scheduled for completion in the Summer of 2021. The entire project is being performed by MEJA Construction and was designed by J.W. Robinson Associates.



Jonesboro High

Targeting a Spring 2021 completion, Phase 2 of the Jonesboro High project is forging ahead. CMU and split face installation are both now complete and window installation is underway. HVAC, electrical and plumbing rough-ins are near completion. Roofing has just begun with lightweight concrete recently starting and HVAC installation will follow. Once complete, the media center and corridor will receive their curtainwall and glass installation and prepare for finishes. In Phase 3 Northwest, the connecting corridor from Phase 2 to the original Jonesboro High has been opened and created with the start of demolition, where roofing and new HVAC has already been completed. With these items complete, the old red paneling will now be removed and new metal panels will be installed. Additionally, this phase will gain classrooms and the new MDF. Over on Phase 3 Southeast, the curtainwall and glass has been installed at Main Street and ceiling grid and drywall installation is taking place. Over the next few weeks finishes such as painting and flooring will begin along with lighting for yet another portion of this vast project to be released to CCPS. The entire, wonderfully Cooper Carry designed, Jonesboro High project is scheduled for completion in the Summer of 2021.

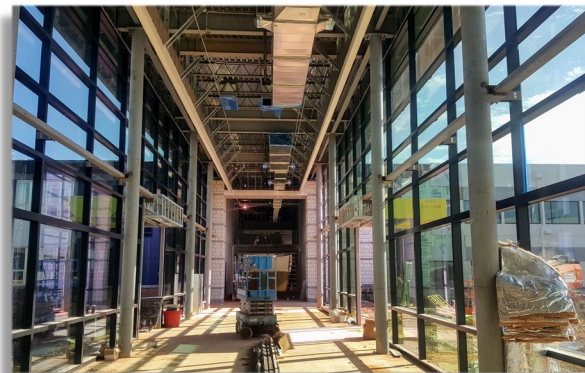

Upcoming Projects

As the Clayton County Public Schools' Construction Department continue to manage current projects, they are planning for the future as well. Please continue to check our district's Construction Department website for upcoming projects as well as information on SPLOST, project updates and monthly progress photos of current projects!

